

Agenda City Council Committee of the Whole

Tuesday, March 26, 2024 at 5:00 PM City Hall Cowles Council Chambers In-Person & Via Zoom Webinar

Homer City Hall

491 E. Pioneer Avenue Homer, Alaska 99603 www.cityofhomer-ak.gov

Zoom Webinar ID: 953 097 829 Password: 234696

https://cityofhomer.zoom.us Dial: 346-248-7799 or 669-900-6833; (Toll Free) 888-788-0099 or 877-853-5247

CALL TO ORDER, 5:00 P.M.

AGENDA APPROVAL (Only those matters on the noticed agenda may be considered, pursuant to City Council's Operating Manual, pg. 6)

CONSENT AGENDA

REGULAR MEETING AGENDA

DISCUSSION TOPIC(S)

- a. BDO Presentation of FY22 Financial Statements Bikky Shrestha, Assurance Partner
- Ben Walters Sidewalk Project Update Leon Galbraith, City Engineer/Special Projects Coordinator

COMMENTS OF THE AUDIENCE

ADJOURNMENT

Next Regular Meeting is Monday, April 8, 2024 at 6:00 p.m. All meetings scheduled to be held in the City Hall Cowles Council Chambers located at 491 E. Pioneer Avenue, Homer, Alaska.

Ben Walters Lane Sidewalk Improvements Status

Leon Galbraith, P.E.

City Engineer

3/19/24

Project History

- Ordinance 21-36(S-2)(A): 160 HART Roads Design/Survey
- Ordinance 23-23(A-3): 160 HART Roads Construction
- Request for Proposals Consultant Design Services HDL selected to complete design

Project Finances

- Ben Walters Sidewalk - \$100,000 for design/survey services (under budget so far), \$1,700,000 for construction 2024

PRV Design/Construction added – Ordinance 23-64 estimated cost \$300,000 funded from Water CARMA

<u>Current Professional Design Services Status</u>

Managing 3 consultant contracts: HDL, RESPEC, and Kinney Engineering


- Ben Walters Lane Sidewalk Improvements (100%) HDL, Project No. 160-0798-XXXX
- Ben Walters PRV Station (95%) RESPEC \$45,000 design contract, PW design task order #24-01
- Ben Walters Lane TCE/TCP acquisition Kinney Engineering \$4,000 PW design task order #23-06



Ben Walters Lane Sidewalk Improvements

- 10' wide asphalt sidewalk on east side
- 2" thick pavement & D-1 & subbase & geotextile
- Curb and Gutter w/ SD inlets
- ADA parallel curb ramps w/ tiles at approaches
- Driveway curb cuts with ADA ramps


- Utility adjustments (W/SS/SD/ELEC)
- New street signs and posts
- SD cross culverts to daylight drainage
- Remove existing PRV and vault
- New water main and fire hydrants
- TOTAL CONSTRUCTION: \$1,658,620

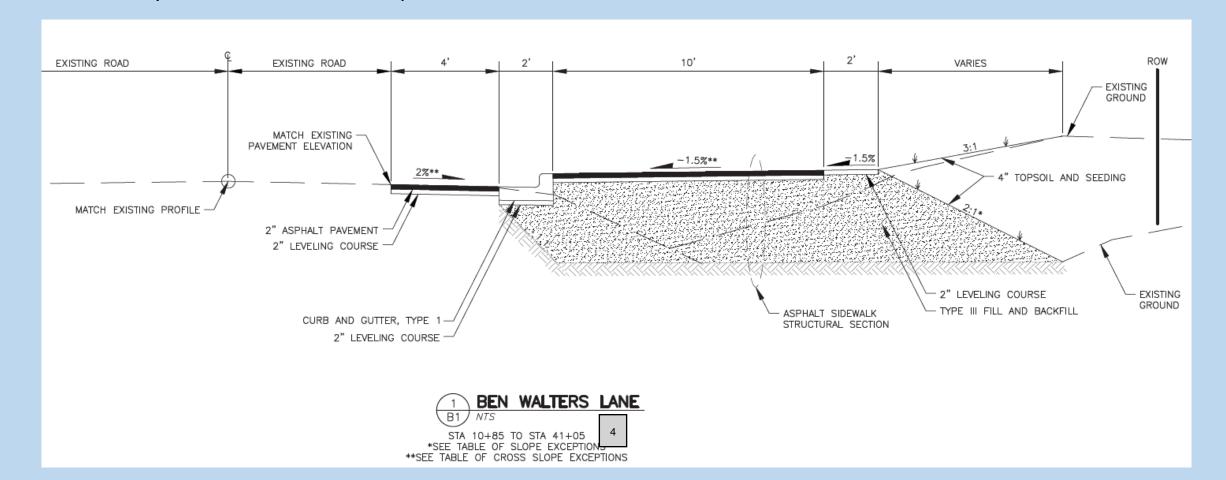


Ben Walters PRV Station

- At 95% design level
- Need an EOQ and Eng. Cost Estimate
- RESPEC currently addressing COH design review comments
- ADEC coordination and review

- Above grade shed within ex utility easement
- Complex design includes architectural, civil, structural, Mechanical and electrical elements and connections
- TOTAL CONSTRUCTION: \$?

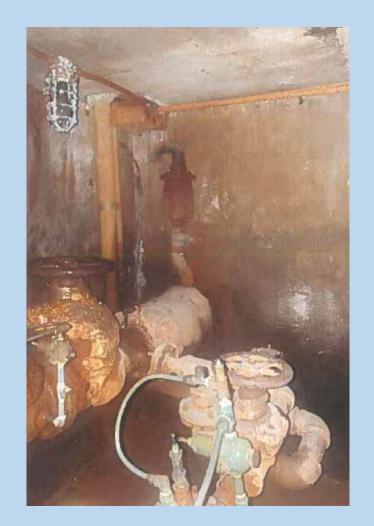




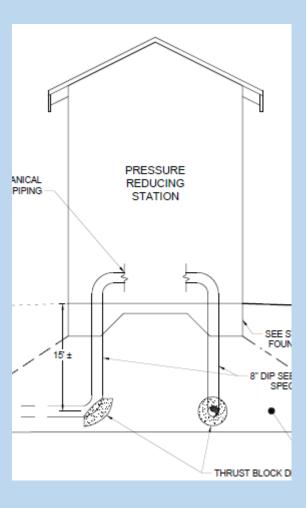

Ben Walters Lane TCE/TCP Acquisition

- Outreach to property owners throughout corridor
- In person contact and signature pages acknowledging private property impacts
- No \$\$ for these easements/permits
- 15 individual ROW permits, 9 individual properties
- Expected to wrap up task by end of April

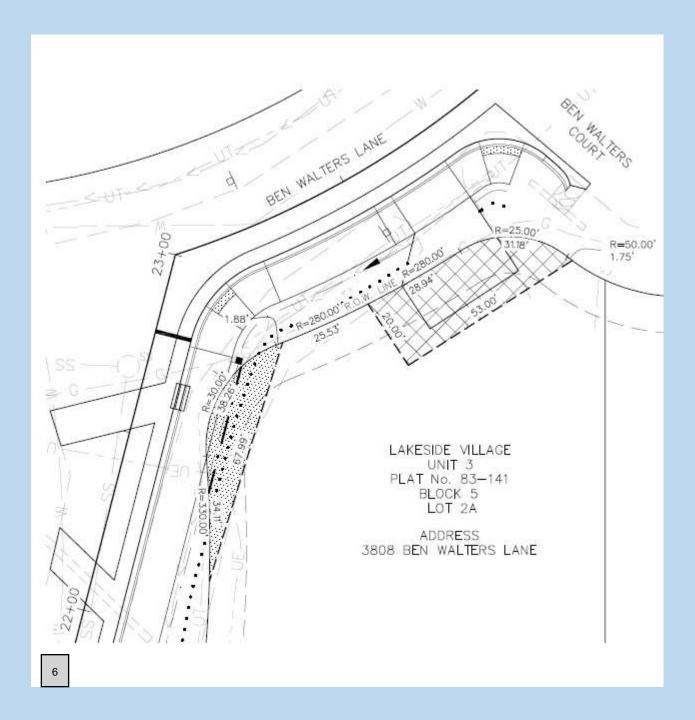

Next Steps

- Provide final Plans/Specifications/Cost Estimate review comments to all 3 consultants
- Coordination with and receive signed and sealed bid docs and permits from all
- Receiving invoices and paying for our consultant professional services
- Bidding/Advertising Package Prep
- Project award and construction kickoff summer 2024
- Project inspection and construction documentation and processing RFI / change orders
- Project closeout
- QUESTIONS?

