



CITY OF NOVI
Administrative ePacket
March 20, 2025

Council Action/Attention

[Plante Moran Realpoint Update](#)

Departmental Updates

[The Buzz Report](#)

[Open Drain/Ditches Asset Management - Wiktorowski](#)

[2024 Engineering Report - Runkel](#)

[Appreciation Events - Walsh-Molloy](#)

For Your Information

[RRRASOC 2025 Household Hazardous Waste \(HHW\) Postcard](#)



City of Novi - Project Status Overview

Status Summary

Novi City Council Weekly Update #9

As of:

3/19/2025

Overall
Status

In progress

PMR Previous Activities (October 2024 – March 2025)

~~PMR Request for additional due diligence (1/27/25)~~

- ~~• (Environmental reports; Geotechnical; Utilities; Legal Descriptions) for all three sites plus road construction work. FS #4 budget to be created.~~

Facility Conditions Assessment (PMR deliverable - in progress, due April)

- FS #4 added

Education Plan (in progress)

Site Selection (PMR deliverable – in progress):

Upcoming Activities

Refine Cost Estimates (PMR – Complete for 3/10 Council meeting)

- FS #4 improvements to be identified with city per its request on 2/28/25

Royal Oak PD / W. Bloomfield FS Tour to be rescheduled

Education Plan

- PMR providing support for the City
- City landing webpage to go live 3/21/25

Request For Proposals

- PMR drafting RFPs for A/E and CM

Areas for Discussion

Site Due Diligence / Budget Items Checklist:

- Improvements to FS #4 added to project scope. Further refinement needed with City to determine FS #4 budget. \$2 million allowance has been budgeted
- City / PMR to review Due Care Plan and strategize path forward

Fire Station #2 Site:

- PMR pursuing alternative sites and conducting test fits

Education Plan Roles and Responsibilities:


- City of Novi to lead all elements of the educational plan
- PMR will provide editorial support as needed upon request
- Webpage to go live 3/21/25 for State of the City
- PMR to provide Facility Assessment Executive Summary for website

Upcoming Administration Meeting: 3/24/25

After 3/24, future City/PMR meetings will occur monthly

Buzz Report

March 24, 2025



Hot Topics:

- **2025 Road Construction Projects Map**

A new map featuring all currently planned 2025 Road Construction Projects has gone live on the city website. The map is color coded to identify the type of project and includes the official detour routes for each project in lefthand panel. Any changes and updates to the road projects will be reflected in the map as needed, typically within the week of the update.

- **Novi High School Tennis Lights**

The High School has turned on the lights in the tennis courts for the season. While no complaints have yet been received, this historically has caused some curiosity and consternation from neighboring residents.

- **Shawood Lake Island Purchase**


The purchase agreement for the Island has been signed. Title paperwork is being worked on by the attorneys of both parties, and we are awaiting the property survey.

- **City Water Chlorine Concerns**

Last weekend (March 8-9), in the online community for Ring Camera owners, there was a question posed about a strong chlorine smell/taste for water, particularly in the north end. A few others commented on it as well, some that resided outside the City. However, the Department of Public Works Water & Sewer Division reported that Chlorine levels at the West Park storage facility were at 1.27 ppm, which is within the normal range. Residents who have issues are welcome to request a site visit for us to test the Chlorine residuals

- **Sanitary Sewer Interceptor Repair Project – Use of City Property**

As a result of the action [Council took on January 6th](#) to participate in the cost share to make improvements to portions of Huron Rouge interceptor, crews working on the project will be using the property at the corner of Bond and Grand River for the next year to assist in mobilization in conjunction with their project.

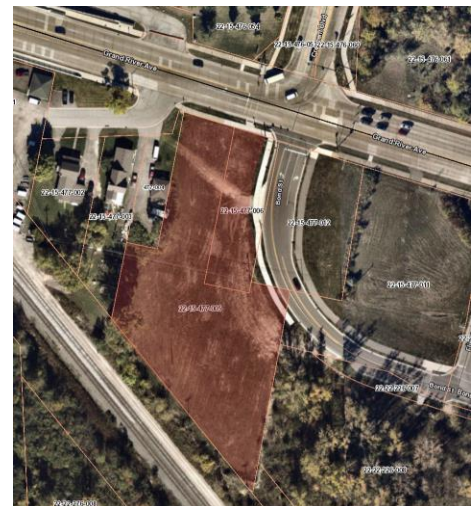

- **Taft Road Trees**

There has concern about the number of trees wrapped with yellow tape along Taft Rd between 9 Mile and 10 Mile. City Forester Keith Salowich spoke with Consumers Energy and it was confirmed that there was simply a miscommunication with the crew that was marking trees and they mistakenly wrapped far more trees than necessary. In reality, there are only a few very small trees that are at risk of being impacted, and that can likely be transplanted elsewhere. All the rest of the trees will be left alone and their crew will be removing the excess tape from those.

Development Project Updates:

Map of Development projects

- **Station Flats**

The planned project in between Target and Sam's has been scuttled and there are no proposals to continue with it in its current form

- **Camelot Parc/Avalon** by Village of Stonebrook

Town homes for sale with garages, fewer units (currently zoned under a special land use, which council will have a decision)

- **On the Border (Haggerty Road) Closed**

UPDATE - Per earlier updates please see the following [article about a chapter 11](#) filing by the corporate On the Border holding company.

- **Porsche of Novi** – Grand River/Haggerty Road

UPDATE – A Temporary Certificate of Occupancy (TCO) has been issued for the 19,170 square foot, two-story Porsche car dealership (next to the Audi Sales Center)

- **El Car Wash # 2 will take over the Original \$6 Car Wash on Novi Road and 96**

- **Audi Sales Center** (Former Jaguar dealership) – 10 Mile/Haggerty Road

The former Jaguar dealership located at 24295 Haggerty Rd is in the process of being converted to an Audi Sales Center. Currently the renovation is in full swing and recently was approved for its "rough" building inspection.

Estimated Completion Date: Mid-April 2025

- **Elm Creek PRO (Meadowbrook and 12 Mile development)**

The residential development [proposed by Toll Brothers](#) (two-phased 134-unit multiple-family townhome development) has been halted, and they will not be proceeding with construction. It would appear this is a result of a property dispute between the owners of the parcel.

- **[Joann CLOSING](#)**

The fabric and craft retailer Joann filed for bankruptcy for a second time in January and this Wednesday (2/19/25) announced plans to close approximately 500 of their stores across the nation, 37% of these closures are in the Great Lakes region. **Included** in the list of planned store closures is the longtime Novi location in West Oaks (next to Kohl's).

- **El Car Wash** (Former PNC Bank) – Grand River Ave/12 Mile Rd

The former PNC Bank located at 48648 Grand River Ave has been demolished and an El Car Wash will be being built on the site. The project has already received approvals from the Planning Commission (4/10/24) and Zoning Board of Appeals (5/14/24). Currently, a pre-construction meeting has been held and the building plans are in the final stages of review prior to permit issuance.

Estimated Completion Date: Fall 2025

- **Cantaritos Fiesta Mexican Restaurant** (Former Chili's Grill & Bar) – 8 Mile/Haggerty Road
The former Chili's location in the City's southeast corner is planned to soon become a new Mexican restaurant following necessary renovations and upgrades to the interior of the building. The restaurant also has a location in Royal Oak that opened in May 2023. The building plans for the renovation were recently submitted and undergoing review.

Estimated Completion Date: Late Spring or Summer 2025

- **Raising Cane's Chicken Fingers** (Former Wendy's) – Novi Rd/Grand River Ave
The Novi Wendy's location at 26245 Novi Rd recently closed as part of a company plan to shutter 140 locations nationwide. The Louisiana-based fast food chain Raising Cane's is planning to take over the space in the near future. Raising Cane's specializes in chicken fingers, crinkle-cut fries and Texas toast.

Estimated Completion Date: Currently Unknown (no submittals to date, project scope unclear)

- **Primrose School** (Former Whitehall nursing home) – 10 Mile/Novi Road
The former Whitehall nursing home at 43455 Ten Mile Rd has been demolished and Primrose School, a 13,586 square feet private preschool and daycare center, is currently being built on the former site. When completed, is estimated to be able to have 202 children during its peak hours.

The construction was previously limited only to foundation/flatwork while a hydrant was installed to make water available at the site. As of December 4th, the full building permit has been issued which will allow them to proceed with "vertical" construction.

Estimated Completion Date: Summer 2025

Frequently Asked Questions:

None at current

MEMORANDUM




TO: JEFFREY HERCZEG, DIRECTOR OF PUBLIC WORKS
FROM: MATT WIKTOROWSKI, FIELD OPERATIONS MANAGER
SUBJECT: OPEN DRAINS (DITCHES) ASSET MANAGEMENT
DATE: MARCH 20, 2025

The DPW Field Operations Division is responsible for not only the routine maintenance of Novi's roadways but also for ensuring the effective operation of the community's stormwater system. Annually, the Division allocates over \$500,000 for the preservation of this aging infrastructure through contracted services, alongside an average of \$600,000 for labor and materials using City personnel and equipment.

While a considerable portion of the City's stormwater system is located underground (e.g. neighborhood catch basins and gravity mains), there remains a substantial network of visible assets classified as open drains or ditches. These stormwater conveyance swales were previously not seen as assets and subsequently overlooked as stormwater maintenance programs were developed. However, in recent years we have seen an increase in failed culverts, sedimentation, and vegetation encroachment. Rather than react to areas with reported flooding when these conditions were reported, staff moved to a proactive approach to the maintenance program.

Two years ago, DPW Field Operations completed field verifications to determine the exact locations of the City's open drain assets. After the assets were field verified, GIS integrated the inventory into the City's mapping system. Adding these assets into the system helps staff understand how the overall network functions in conjunction with sedimentation basins, streams, and rivers.

The field verification yielded that the community has approximately 15 miles of public ditches, 1,600 culverts, and 44 spillways requiring regular maintenance.

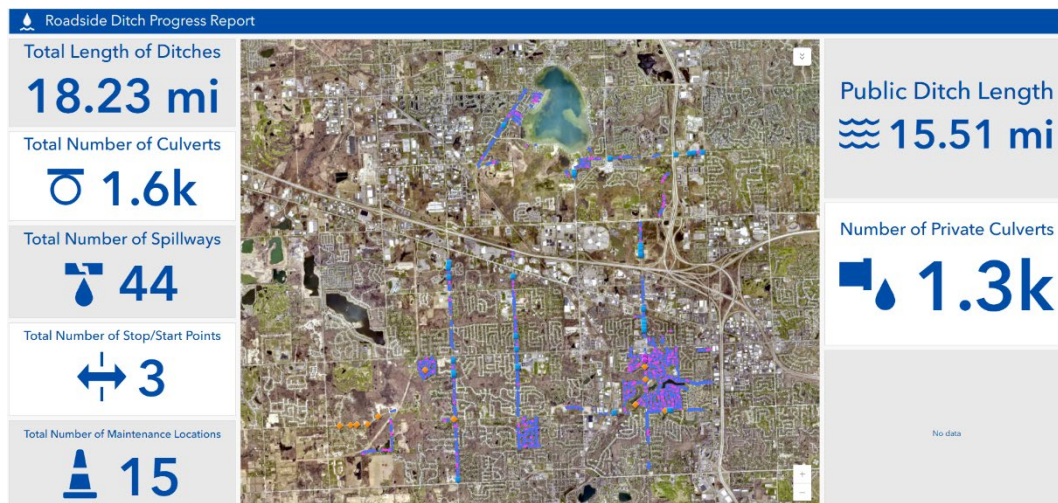

After collecting location data, DPW Field Operations developed an inspection report in Cityworks. Over time, the criteria and condition categories were refined to ultimately look like the following template.

These inspections, conducted annually, encompass several key criteria, including:

1) Flow measurement to identify areas susceptible to flooding;

2) Structural evaluations to effectively plan for material acquisition and equipment requirements; and

3) Assessment of vegetation to determine if the area requires regular mowing or if invasive species need to be addressed before any excavation work.

Based on inspection results, our team creates work orders that can be filtered and scheduled based on asset condition and location. Areas that regularly experience flooding are geographically addressed first.

Location: 41900 Thirteen Mile Rd		
Status: Open	Resolution:	
Insp. Date: 04/3/2024 8:55 AM	Inspected By: TATE, MIKE	
Observations		
Ditch Volume		
☐ High Volume (Culvert >24") ☒ Low Volume (Culvert <=24")		
Capacity - Ditch Flow		
☐ Good - Ditch flows freely, no debris build-up evident ☒ Moderate - Ditch flows freely, some minor build-up evident ☐ Poor - Ditch functions to <25% of capacity		
Capacity - Flooding		
☐ Good - No evidence of localized flooding ☒ Moderate - Not applicable ☐ Poor - Evidence of localized flooding		
Structural Components - Damage		
☒ Good - No damaged components present ☐ Moderate - Damaged components, but not causing flow blockages ☐ Poor - Damaged components causing flow blockages		
Structural Components - Debris		
☐ Good - No debris buildup at inlet or outlet ☐ Moderate - Debris buildup at inlet or outlet blocking 25% of inlet/outlet capacity ☒ Poor - Debris buildup at inlet or outlet blocking 50% of inlet/outlet capacity		
Vegetation - Bottom Coverage		
☒ Good - Covering 90% of ditch bottom ☐ Moderate - Covering 75-90% of ditch bottom ☐ Poor - Covering <75% of ditch bottom and/or causing line-of-sight issues		
Vegetation - Mowing		
☒ Good - Recently mowed (<1 year ago) ☐ Moderate - Mowed last year (2 years ago) ☐ Poor - Not recently mowed (3 or more years ago)		
Vegetation - Weeds		
☒ Good - No noxious weeds present ☐ Moderate - Noxious weeds present, but are actively being managed ☐ Poor - Noxious weeds present and not being managed		
Integrity - Bare Spots		
☒ Good - No bare spots ☐ Moderate - 10-20% bare spots ☐ Poor - >40% bare spots		
Integrity - Illicit Activity		
☒ Good - No evidence of nuisance animals ☐ Moderate - Evidence of illegal dumping ☐ Poor - Evidence of nuisance animals or illicit connections		

A key piece of equipment used to perform this work is a mini excavator. For several years, DPW had one unit, which was shared by crews to maintain storm drain and roadway assets, and other projects requiring small implements and minimal weight allowances. After the initiation of this program, an additional unit was specified and purchased which is equally as versatile as the original but has a greater reach to allow for deeper digging depth. This feature provides operators with the ability to expand the roadside ditching service provided to our residents through job efficiency and productivity; two crews can work at separate ditching locations. The Field Operations Division had previously been renting a comparable excavator every year for the last five years (spending on average \$15,000/year) to complete the drain ditching and other stormwater projects.

Open drains are often underestimated as vital components of community stormwater management. When these areas are compromised, flooding can occur, resulting in damage to both private and public properties. City Council's continued support to purchase the proper equipment and materials is integral in the implementation of this program, which will significantly benefit our residents, motorists, and the environment.

The following pictures demonstrate some of the work our team performs each season to maintain this open drain network.



Removing and replacing culverts between ditches



Cleaning a ditch full of sediment



Inspecting high water volume culverts before making structural repairs



MEMORANDUM

TO: JEFFREY HERCZEG, DIRECTOR OF PUBLIC WORKS
FROM: REBECCA RUNKEL, PROJECT ENGINEER
SUBJECT: 2024 ENGINEERING DIVISION ANNUAL REPORT
DATE: MARCH 20, 2025

Novi's Engineering Division oversees the design and construction of public infrastructure improvements within the City. The Engineering Division also reviews and inspects private development projects from conception to post-construction. Engineering staff work closely with residents, consultants, local/state agencies, contractors, developers, and other City Departments to facilitate the completion of successful projects.

Engineering Division Duties

In 2024, the Engineering Division consisted of seven full-time professionals. The Engineering team reviews private development site plans, public infrastructure plans, and oversees private and public infrastructure construction.

Below are the 2024 team members and their primary responsibilities:

- Ben Croy, PE; City Engineer – responsible for overseeing the Engineering Division and serves as the City's Traffic Engineer.
- Aaron Staup; Construction Engineer – responsible for the construction phase of public infrastructure projects.
- Rebecca Runkel; Project Engineer – responsible for the design phase of public infrastructure projects.
- Humna Anjum; Project Engineer – responsible for engineering plan review and the construction phase of private development projects.
- Ben Nelson; Project Engineer - responsible for engineering plan review and the construction phase of private development projects.
- Jeff Van Curler; Engineering Technician – responsible for right-of-way permitting and inspections, and various engineering tasks as assigned.
- Milad Alesmail; Project Engineer - responsible for engineering plan review and the construction phase of private development projects.

Annual Overview

The main responsibilities of the Engineering Division are detailed in this section. The following table provides a summary of the Engineering Division's activities during 2024:

Activity	2023	2024
Grant Funding Obtained	\$287,777	\$706,354
Private Site Plan Reviews	124	121
Final Site Plan Approvals	32	25
Right-of-Way Permits Processed	208	229
Soil Erosion Permit Reviews Completed	45	57
Private Development Pre-Construction Meetings Held	13	19
Private Development Utilities Accepted	2 affidavits	5 affidavits
Private Development Streets Accepted	7 segments	1 segment
New Street Light Installations	0	1
Average PASER Rating	5.8	6.0
Number of Capital Construction Projects Substantially Completed	12	9
Dollar Value of Capital Construction Projects Substantially Completed	\$22,701,484	\$23,805,984

- ### Grant Funding

In April 2024, the City was awarded \$578,897 in Federal funding through Michigan Department of Transportation's (MDOT's) Transportation Alternatives Program (TAP) for construction of a connector pathway between the ITC Trail and Bosco Fields Park. The City also received \$127,457 in funding through Oakland County's 2024 Local Road Improvement Program that went towards the rehabilitation of 13 Mile Road between Meadowbrook Rd and M-5 (see page 7).

- ### Private Development Site Plan Review

Plan reviews for private development are completed by in-house City Engineering Staff, saving upwards of \$80,000 per year in engineering consulting fees. In 2024, the Engineering Division reviewed 121 private site plans; of which 25 final site plans were approved. Site plan submittals come in the form of pre-applications, preliminary site plans, and final site plans.

- ### Private Development Construction

The Engineering Division hosted 19 pre-construction meetings for private developments. Staff managed site inspections, legal document reviews, and responded to community inquiries. The City accepted 5 affidavits for water and/or sanitary sewer systems from developments for the year. The City accepted one public street segment from private developments in 2024.

- **Soil Erosion and Sedimentation Control Permit Review**

All full-time City engineering staff are certified for Soil Erosion and Sedimentation Control (SESC) reviews. Bringing reviews in-house saves the City anywhere from \$300 to \$800 in consultant review fees per site. Engineering staff are responsible for the review and approval of all soil erosion and sedimentation control (SESC) permits associated with site developments and public projects. There were 57 SESC permit applications reviewed for private development projects and 6 SESC permits issued for the City's public infrastructure projects.

- **Right-of-Way Permitting**

Staff reviewed 229 right-of-way applications for franchise utility installation (electric, gas, fiber), private development projects, residential driveway replacements, and other miscellaneous work in the right-of-way. The right-of-way permitting process minimizes impact to public water mains, sanitary sewer, storm sewer, ditches, roads, sidewalks and verifies that restoration within the public right-of-way is completed per City standards.

- **Capital Improvements Program (CIP)**

Engineering staff develops and manages multiple projects relating to roads, intersections, pathways, storm water, sanitary sewer, and water distribution sections as outlined in the City's Capital Improvement Program. Preparation for each project includes detailing the project scope, justification, public benefits, and cost estimates that include any necessary right-of-way acquisition, design, geotechnical services, etc. Please refer to the list of capital projects presented beginning on Page 4.

- **Street Lighting**

Each year, engineering staff works with homeowner's associations (HOAs) and developers to facilitate the installation of street lighting by DTE Energy. The Street Lighting Policy states that the City will pay for the installation and ongoing annual costs of a single standard streetlight at each subdivision entrance on a major street. One new streetlight was added in 2024 at the Parc Vista subdivision entrance.

- **Transportation Asset Management**

The Pavement Surface Evaluation and Rating System (PASER) is one component of the City's asset management approach. PASER ratings are on a scale from 1 to 10, with 10 being the best (road does not require any maintenance) and 1 being the worst (road has failed and requires reconstruction).

The average PASER rating is an indicator of the overall condition of the road pavements within the City network. City roads are rated every two years. The last rating occurred in November 2024. Roads that are under the jurisdiction of the governing county/road agency were excluded from the evaluation. The table on the next page shows PASER ratings from the last 10 years. City roads will be rated again in fall 2026.

PASER by Year

Evaluation Year	2013	2014	2015	2017	2018	2019	2020	2022	2024
Average PASER Rating	5.9	5.6	5.6	5.5	5.5	5.5	5.8	5.8	6.0

2024 Public Projects

Neighborhood Roads Program

The Neighborhood Roads Program (NRP) consists of asphalt and concrete rehabilitation and reconstruction of local roads. AECOM assisted the Engineering Division with preparing a list of streets for the 2024 and 2025 Neighborhood Roads Program (NRP). The program is divided into two contracts: one focusing on concrete roads, and the other focusing on asphalt roads. The program was advertised as a two-year contract to lower the overall cost of bidding and design, and to lock in unit prices. The two-year contract also allows the City flexibility in scheduling the different project areas.

2024 NRP – Concrete Streets

The construction contract was awarded to Mattioli Cement Company. The project included reconstruction of the streets listed below, which were completed in 2024.

Street Segment	From	To	Treatment
Argyle St	Whitehall Dr	Broadmoor Park Ln	Full Reconstruction
Broadmoor Park Ln	Argyle St	End of Cul-de-sac	Full Reconstruction
Broadmoor Park Ln	Northumberland St	Baker St	Full Reconstruction
Whitehall Dr	White Pines Dr	Argyle St	Full Reconstruction
Venice Dr	Roma Ridge Dr	End of Cul-de-sac	Full Reconstruction

Engineering Consultant: AECOM
Construction Contractor: Mattioli Cement Company

Original Contract Price: \$ 1,018,819
Current Contract Price: \$ 1,016,909

Project Start Date: June 25, 2024
Substantial Completion Date: October 23, 2024

2024 NRP – Concrete Streets, continued

Broadmoor Park Ln & Argyle St- Before



Broadmoor Park Ln & Argyle St- After



2024 NRP – Asphalt Streets

The construction contract was awarded to Pro-Line Asphalt Paving Corporation. The project included reconstruction of the streets listed below, which were completed in 2024.

Street Segment	From	To	Subdivision
Sunday Dr	Hillside Dr	Park Place Dr	Park Place
Waterland Dr	Park Place Dr	End	Park Place
Applebrooke Dr	Roberts Rd	End	Park Place
Berwick Ct	Applebrooke Dr	End	Park Place
Vasilios Ct	9 Mile Rd	End	Vasilios Estates

Engineering Consultant: AECOM
Construction Contractor: Pro-Line Asphalt Paving Corporation

Original Contract Price: \$ 1,947,719
Current Contract Price: \$ 1,947,719

Project Start Date: April 24, 2024
Substantial Completion Date: November 1, 2024

2024 NRP – Asphalt Streets, continued

Waterland Dr - Before



Waterland Dr - After



13 Mile Road Rehabilitation, Meadowbrook Road to M-5

In 2020, the City entered into a cost-share agreement with the Great Lakes Water Authority (GLWA) to reconstruct four road segments following the construction of a 54-inch transmission water main between 8 Mile Rd and 14 Mile Rd. After numerous setbacks which extended the construction timeline for the GLWA project, the City opted to complete the road rehabilitation along the 13 Mile Rd segment, between Meadowbrook Rd and M-5. A change order was issued to the paving contractor, Cadillac Asphalt, LLC, who had two open contracts with the City (Industrial Roads Rehabilitation, Taft Rd Rehabilitation). Issuing the change order to a contractor already working in the City allowed for better control of the paving quality and faster completion.

Engineering Consultant: AECOM
Construction Contractor: Cadillac Asphalt, LLC

Original Contract Price: \$ 927,466
Current Contract Price: \$ 939,601

Project Start Date: June 29, 2024
Open-to-Traffic Date: August 15, 2024

13 Mile Rd - Before



13 Mile Rd - After



Pavement Preservation Overlays

The pavement on Beck Road between 9 Mile Rd and 11 Mile Rd was in poor condition. Due to the uncertainty of the Beck Road widening project and delays in the environmental assessment process, City staff decided to issue a change order to Ajax Paving to do a thin asphalt overlay to extend the life of the pavement and improve driving conditions while waiting for the widening project to take shape. 11 Mile Rd, between Taft Rd and Beck Rd, was added to the project due to its proximity and cost effectiveness compared to a full rehabilitation, which had been in the CIP for FY 2026-27.

Engineering Consultant: AECOM
Construction Contractor: Ajax Paving

Original Contract Price: \$ 1,081,882
Current Contract Price: \$ 1,334,991

Project Start Date: August 8, 2024
Project Completion Date: August 26, 2024

Beck Rd – Before



Beck Rd – After



Wixom Road Rehabilitation, 10 Mile Rd to Grand River Ave

The City was awarded \$1.5 M in federal funds for a Wixom Road rehabilitation project through the Oakland County Federal Aid Committee (FAC) Surface Transportation Program (STP). The project consisted of cold-milling and resurfacing the asphalt pavement, a center left turn lane addition between Drakes Bay Dr/Acorn Tr and Kelsey Bay Dr/Delmont Dr, curb and gutter repairs, sidewalk gap infill and ADA improvements, and drainage structure repairs.

Engineering Consultant: OHM Advisors
Construction Contractor: Fonson Company, Inc.

Original Contract Price: \$ 5,046,141
Current Contract Price: \$ 5,185,659

Project Start Date: March 4, 2024
Open-to-Traffic Date: November 1, 2024

Wixom Rd - Before



Wixom Rd - After




Wixom Road Sanitary Sewer Replacement and Drakes Bay/Wixom Road Pump Station Reconstruction

Two sections of sanitary sewer between the Drake's Bay lift station and Lanny's lift station were identified in the 2014 Sanitary Sewer Capacity Assessment as having insufficient capacity to handle current and future flow rates. This project replaced 1,200 feet of 18-inch diameter sewer with 21-inch diameter sewer, and 1,600 feet of 12-inch sewer with 15-inch sewer to increase capacity. Pipe bursting was used where possible to avoid further disruption to area residents. Additionally, the sanitary pumps and generators in the Drake's Bay and Wixom pump stations were replaced to better handle the flow rates.

Engineering Consultant: Spalding DeDecker
Construction Contractor: Pamar Enterprises, Inc.

Original Contract Price: \$ 5,553,937
Current Contract Price: \$ 5,408,928

Project Start Date: July 17, 2023
Open-to-Traffic Date: April 17, 2024

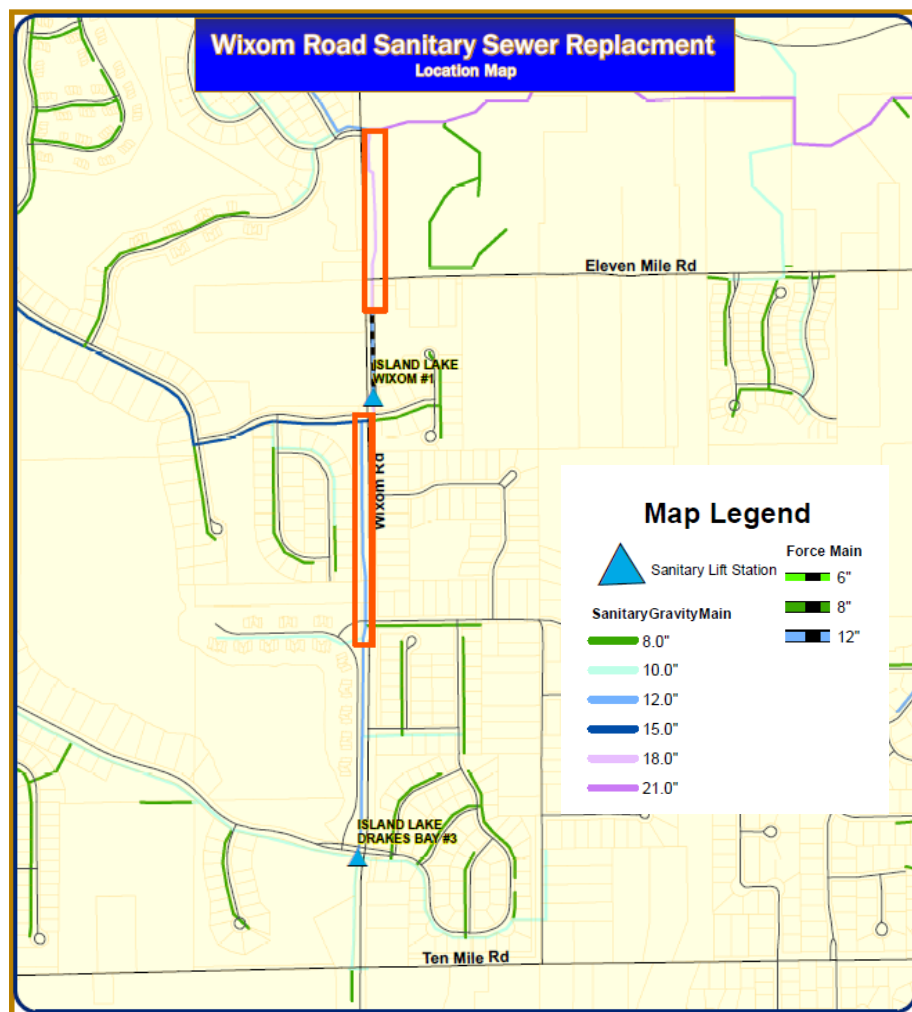

2024 Neighborhood Sidewalk Repair Program

Following the completion of the pilot sidewalk repair program in Meadowbrook Glens, the Engineering Division, with the help of AECOM, developed a plan for a second program. The second program repaired sidewalks in five subdivisions: Chase Farms, Willowbrook Farms, Bristol Corners, Yerkes Manor, and Westminster Village. Sidewalk panels were evaluated for cracking, deflections, and surface deterioration, and were replaced based on the criteria of having a $\frac{3}{4}$ -inch deflection or greater, 25% or more surface cracking/deterioration, or as deemed necessary by the engineer. Additionally, trees adjacent to sidewalks were evaluated for pruning or removal.

Engineering Consultant: AECOM

Construction Contractor: Hartwell Cement Company

Original Contract Price: \$ 435,038

Current Contract Price: \$ 497,117

Project Start Date: August 13, 2024

Substantial Completion Date: December 14, 2024

Bristol Corners



Jessica's Splash Pad

Jessica's Splash Pad was opened on May 25, 2024, at Bosco Fields Park (Beck Road south of 11 Mile Rd). The splash pad honors former FOX 2 meteorologist and Novi resident, Jessica Starr-Rose, who died in 2018. Novi's City Council, PRCS, and DPW worked together with the Starr-Rose Family and the Novi Parks Foundation to bring the project to fruition. The 4,500 square foot splash pad includes a recirculating water system, a new restroom and changing facility with a 20-ft x 20-ft mechanical room, a pedestrian bridge, a concrete plaza with shade structures and seating, and landscaping/fencing.

Engineering Consultant: OHM Advisors
Construction Contractor: DeAngelis Diamond Construction

Original Contract Price: \$ 1,931,416
Current Contract Price: \$ 2,096,004

Project Start Date: June 12, 2023
Substantial Completion Date: July 27, 2024



Meadowbrook Commons Pickleball Courts and Parking Expansion


Due to the growing popularity of pickleball, the PRCS department sought opportunities to construct more pickleball courts in Novi. PRCS received a \$150,000 grant from the Oakland County Senior Centers Grant Program for development of pickleball courts at Meadowbrook Commons Activity Center. Four pickleball courts were constructed at the northeast corner of the property, and included benches, shade canopies, and walkways from the parking lot. Additionally, the main parking lot was expanded to accommodate more vehicles. The project was bid together with the Wildlife Woods Pickleball Courts and Parking Expansion project.

Engineering Consultant: Spalding DeDecker
Construction Contractor: T&M Asphalt Paving, Inc.

Original Contract Price: \$ 550,924
Current Contract Price: \$ 539,972

Project Start Date: April 9, 2024
Substantial Completion Date: July 18, 2024

Before

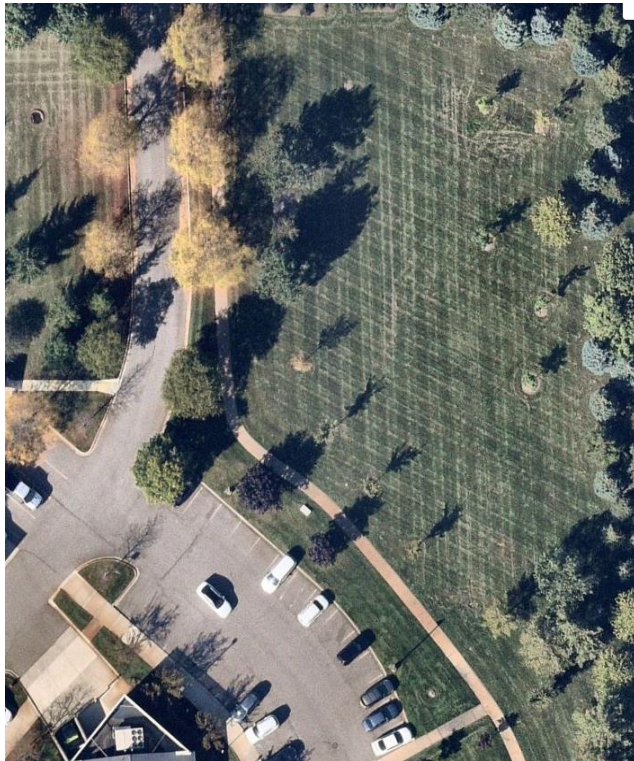

After



Wildlife Woods Pickleball Courts and Parking Expansion

Wildlife Woods was home to Novi's first four pickleball courts, which were constructed in 2020. Due to frequent use and growing popularity of pickleball, PRCS decided to add an additional four courts to Wildlife Woods. The parking lot at Wildlife Woods was also expanded to accommodate more visitors. The project was designed and bid out in conjunction with the Meadowbrook Commons Pickleball Courts and Parking Expansion project.

Engineering Consultant: Spalding DeDecker
Construction Contractor: T&M Asphalt Paving, Inc.

Original Contract Price: \$ 565,227
Current Contract Price: \$ 580,278

Project Start Date: July 19, 2024
Substantial Completion Date: November 11, 2024

Pickleball Court Construction at Wildlife Woods



Meadowbrook Lake Streambank Stabilization and Dredging

Meadowbrook Lake, in the Meadowbrook Lake subdivision, receives surface water from two inlet tributaries at the north end of the lake. Sediment had built up at both tributaries, leading to the formation of sediment 'islands' in the lake. Hydraulic dredging of 7,000 cubic feet of sediment at the inlets was done, along with 230-feet of streambank stabilization of the Middle Rouge channel leading into the lake south of Chattman Road. The channel had experienced significant erosion, so the streambanks along both sides of the channel were re-graded with installation of rip-rap, coir blocks, soil lifts, and native vegetation.

Engineering Consultant: OHM Advisors
Construction Contractor: M-K Construction Co, Inc.

Original Contract Price: \$ 1,999,454
Current Contract Price: \$ 2,042,085

Project Start Date: November 15, 2023
Substantial Completion Date: March 16, 2024

Streambank – Before



Streambank – After



Meadowbrook Lake – Before Dredging



Meadowbrook Lake – After Dredging



Lakeshore Park Parking Lot Expansion

Lakeshore Park's 10-mile trail network starts at the end of the park's access road. The trails are frequently used by mountain bikers and hikers. The Motor City Mountain Biking Association (MCMBA) has plans to add a changing facility at the trailhead. In advance of the MCMBA project, PRCS staff requested the reconfiguration of the back parking lot. The existing cul-de-sac was removed and additional parking spaces were added to better accommodate visitors to the park.

Engineering Consultant: AECOM
Construction Contractor: True North Asphalt

Original Contract Price: \$ 270,116
Current Contract Price: \$ 264,870

Project Start Date: May 7, 2024
Substantial Completion Date: May 24, 2024

Completed Parking Improvements



13 Mile Road and Novi Road Water Main Replacement

A 2019 inspection of the City's 36-inch prestressed concrete cylinder pipe (PCCP) water transmission main revealed structural deficiencies in four pipe segments. In spring of 2024, the identified segments were lined with carbon fiber reinforced polymer (CFRP). An 8-inch water main was also installed across 13 Mile Rd, just east of Novi Rd to provide additional redundancy. Following the lining portion of the project, staff noticed leaking from a 30-inch butterfly valve at the intersection of 13 Mile Rd/South Lake Dr/Old Novi Rd. The valve will be replaced in early 2025.

Engineering Consultant: AECOM
Construction Contractor: LGC Global, Inc.

Original Contract Price: \$ 1,360,150
Current Contract Price: \$ 1,772,619

Project Start Date: December 19, 2023
Substantial Completion Date: April 15, 2025



Distribution System Material Inventory (DSMI)

The Michigan Department of Environment, Great Lakes, and Energy (EGLE) required all communities complete a Distribution System Material Inventory (DSMI) to determine if any lead or galvanized water service lines exist in the system. At OHM's recommendation, City staff decided to use an existing contract for the work, which was publicly bid by the City of Livonia. It was determined that there are no lead service lines present in the City's water system.

Engineering Consultant: OHM Advisors


Construction Contractor: Underground Infrastructure Services/Duke's Root Control, Inc.

Original Contract Price: \$ 261,712

Current Contract Price: \$ 179,232

Project Start Date: March 25, 2024

Project Completion Date: June 25, 2024

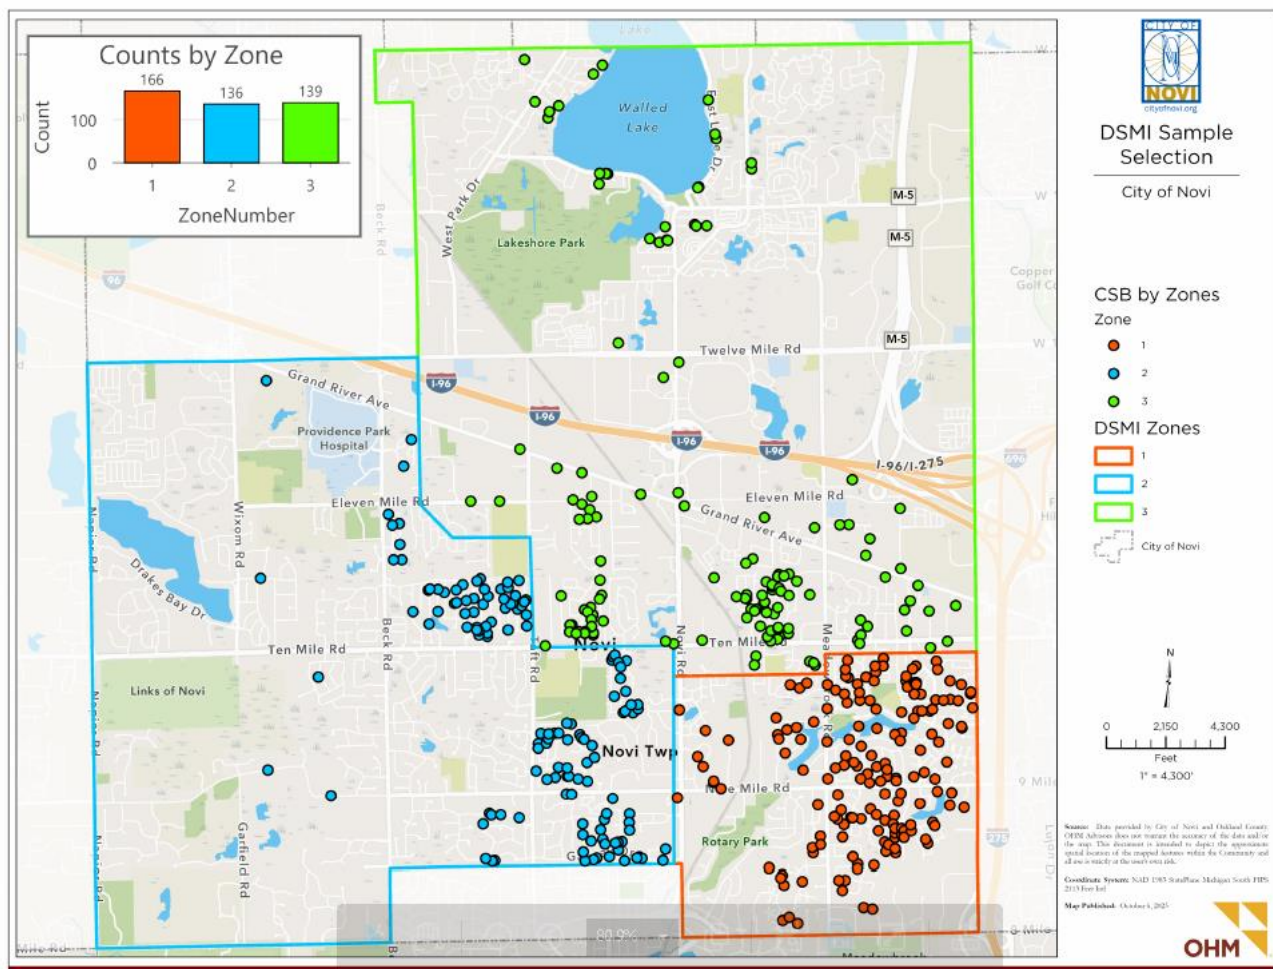

Other Agency Projects


The City of Novi shares the responsibility of maintaining the roads inside the city limits with its neighbors, the Road Commission for Oakland County (RCOC), and Wayne County. The City is also a crossroads for state highways under the jurisdiction of the Michigan Department of Transportation (MDOT). A summary of state and/or county road projects that occurred in 2024 is as follows:

- **Great Lakes Water Authority (GLWA) 54-Inch Water Transmission Main Loop**
GLWA started work in 2022 on construction of a 54-inch transmission water main to interconnect two existing transmission mains at 14 Mile Rd and 8 Mile Rd. The project was completed in October 2024.


GLWA Construction on Meadowbrook Road



- Grand River Avenue, Napier Rd to Wixom Rd Resurfacing (RCOC)**
 This project included major resurfacing and an extension of the center left-turn lane. Construction started in 2023 and was completed in 2024.
- Baseline Road Concrete Pavement Replacement (8 Mile Rd), CSX Railroad to Orchard Hill Place (Wayne County DPS)**
 Phase 1 - Completed 0.87 miles of concrete replacement along with curb ramp work and guardrail replacement from Orchard Hill Place to Woodcreek Blvd.
 Phase 2 - Completed a concrete pavement mill and asphalt overlay from Woodcreek Blvd to the CSX Railroad bridge.
 Phase 3 - Replacement of the bridge deck for the CSX Railroad under 8 Mile during the spring/summer of 2025.
- I-96 Flex Route (MDOT)**
 In 2022, MDOT began construction on a flex lane and ramp metering on I-96 between Kent Lake Road and the 1-275/1-696/M-5 interchange. The flex lane will allow for median shoulders to be used as an additional lane during peak travel times, special events, maintenance activities, and incidents/crashes. The project was completed in November 2024.

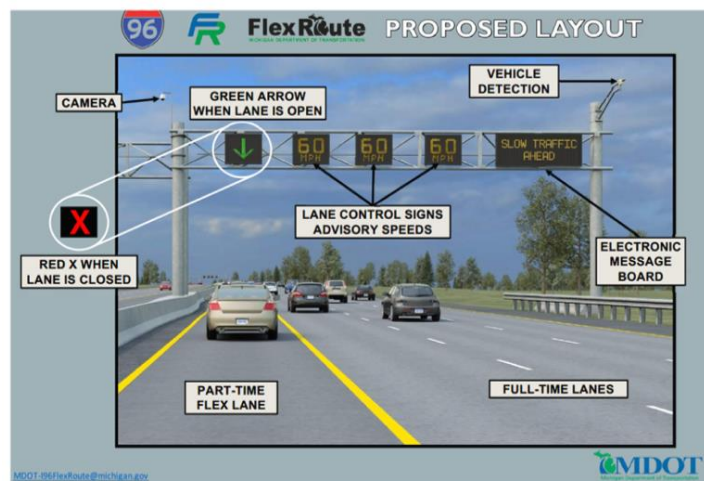

- **Rebuilding Michigan I-696 Project, 1-275 to Lahser Road (MDOT)**
The reconstruction project started in late 2022 and will continue through 2025.

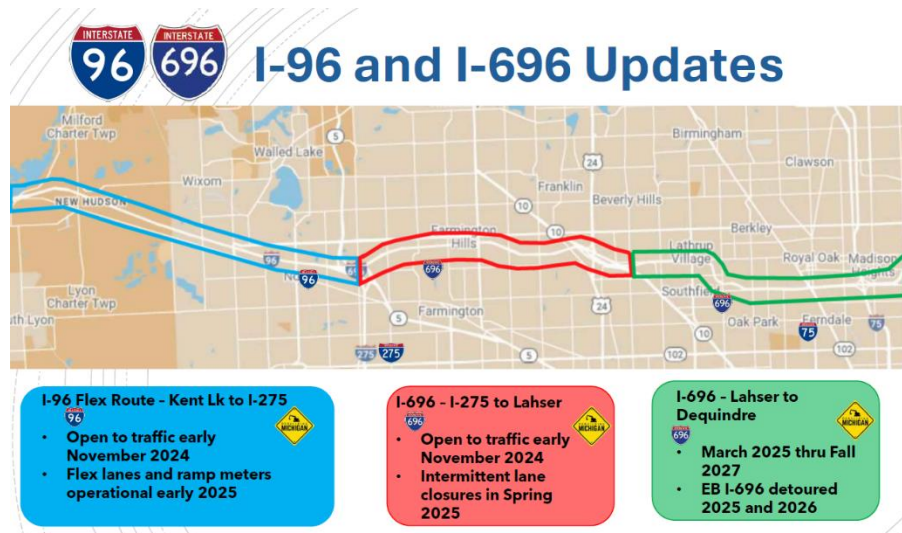

2025 Construction Projects in the City of Novi

The following projects are expected to start or continue construction during 2025:

- **2025 NRP Concrete Streets** – Construction spring/summer 2025
- **2025 NRP Asphalt Streets** – Construction spring/summer 2025
- **2024 CPM** – Chip seal streets, construction spring 2025
- **Nine Mile Road Rehabilitation, Meadowbrook Rd to Haggerty Rd** – Construction spring 2025
- **Meadowbrook Road Rehabilitation, 10 Mile Rd to 11 Mile Rd** – Construction summer 2025
- **Monticello/East Lake Drive Storm Sewer Improvements** – spring 2025 construction
- **Orchard Hills and Leavenworth Detention Basin Improvements** – potential summer/fall 2025 construction
- **13 Mile Road Rehabilitation, M-5 to Haggerty Rd** – summer/fall 2025 construction
- **West Park Drive Rehabilitation, 12 Mile Rd to Pontiac Trl** – potential summer/fall 2025 construction
- **Novi Road Rehabilitation, 8 Mile Rd to 9 Mile Rd, RCOC** – reconstruction between 8 Mile Rd and Allen Dr is planned to start fall 2025. The second phase, rehabilitation between Allen Dr and 9 Mile Dr, will occur in 2026.
- **Novi Road Bridge Preventative Maintenance, over CSX Railroad, RCOC** – TBD 2025
- **Base Line Road (8 Mile Road) CSX Railroad Bridge, Wayne County** – deck replacement and bridge rehabilitation expected to start late 2025.
- **Seeley Drain Culvert Replacement, Haggerty Road between 13 and 14 Mile Roads**

MEMORANDUM



TO: VICTOR CARDENAS, CITY MANAGER
FROM: SHERYL WALSH-MOLLOY, DIRECTOR OF COMMUNICATIONS
SUBJECT: APPRECIATION EVENTS
DATE: MARCH 18, 2025

Following feedback received through an event follow-up survey, we are excited to announce a change to the Annual Appreciation event. This year, the City of Novi will host two separate events to better recognize and celebrate the unique contributions of our dedicated volunteers and hardworking employees.

Survey results highlighted a clear preference for distinct events that allow us to tailor each experience in a more meaningful way. Additionally, employees expressed a strong desire for more opportunities to network with each other, build stronger team connections, and enhance workplace culture. By separating the events, we can:

- Provide a more personalized experience that appropriately honors the efforts of each group.
- Create dedicated opportunities for deeper engagement and connection.
- Foster a stronger sense of teamwork and camaraderie among employees.
- Ensure that both our volunteers and employees feel fully appreciated for their invaluable contributions.

Importantly, these two events will be designed to remain within the current budget allocated for the traditional single event, ensuring we maintain fiscal responsibility while enhancing the experience for all.

Event Details:

- A **Volunteer Appreciation Evening** will focus on recognizing the dedication and service of our volunteers who generously give their time to support our Novi. This event will be very similar to those of the past for the volunteer and a guest, including a buffet and music early in the holiday season. Our team is in the process of developing a formal recognition component to add to this evening.
- An **employee event** will recognize the hard work, dedication, and achievements of our City staff team. The event is anticipated to be held on an afternoon closer to the Christmas holiday.

We believe this change will allow us to better express our gratitude and make each event more memorable and impactful. Details on dates and locations will be shared soon.

2025 Household Hazardous Waste (HHW) Events

HHW Collection Events are open **ONLY** to RRRASOC residents. Electronic waste is accepted and paper shredding is available (up to 3 boxes or 100 pounds) at all HHW Collection Events.

Clothing, shoes, accessories, and small household items will be accepted by Simple Recycling at the events marked with the  icon. Keep separate from HHW. Please bag items when appropriate.

For additional info and accepted materials, visit www.RRRASOC.org or call 248.208.2270.



- | | |
|--|--|
|  Apr. 5 9am-2pm | Wixom Dept. of Public Works
2041 Charms Rd., Wixom |
|  Apr. 26 9am-2pm | RRRASOC MRF - Truck Entrance
20875 Mapleridge Ave., Southfield |
| May 10 9am-2pm | Oakland Community College
27055 Orchard Lake Rd., Farmington Hills |
|  May 17 9am-2pm | Midford Civic Center
1100 Atlantic Street, Midford
Enter from west, off Mont Eagle St. |
|  Jul. 12 9am-2pm | Wixom Dept. of Public Works
2041 Charms Rd., Wixom |
| Oct. 4 9am-2pm | Novi Dept. of Public Works
26300 Lee BeGole Drive, Novi |
|  Oct. 25 9am-2pm | RRRASOC MRF - Truck Entrance
20875 Mapleridge Ave., Southfield |

Did you know?

In 2024, RRRASOC communities recycled **260 tons** of hazardous materials at HHW Collection Events! Disposing of your HHW at a Collection Event eliminates exposure to toxins for children, pets, sanitation workers, and even you! You're also helping to keep toxic materials out of streets, landfills, and bodies of water.



20000 W. Eight Mile Rd.
Southfield, MI 48075

**CONNECT
WITH US:**



E-NEWS
Sign up for e-news
at rrrasoc.org



SOCIAL
facebook.com/rrrasoc



WEB
www.rrrasoc.org



MOBILE APP
for iOS & Android



RRRASOC RECYCLING GUIDELINES



Keep recyclables
EMPTY, CLEAN,
and DRY



DON'T BAG
THEM; leave
them loose



Break down
cardboard boxes
to save space



Return grocery
bags to stores
for recycling

PLEASE RECYCLE THESE



Flattened
Cardboard & Clean
Pizza Boxes



Paperboard Boxes,
Paper Cups, Paper Bags,
& Cartons



Office Paper, Mail,
Magazines, Newspaper,
& Paperback Books



Plastic Jugs, Bottles, & Containers:
#1, #2, #4, #5, #6, #7



Bulky #2
Plastics



Garden
Plastics



Steel/Aluminum
Bottles & Cans



Non-Ceramic
Pots & Pans



Glass Bottles & Jars
(All Colors)

NOT ACCEPTED CURBSIDE OR AT THE DROP-OFF SITES

Check these items on the Recycling Directory at RRRASOC.org for more info.



Plastic Bags & Wrap
Food storage bags, snack
bags, bread bags, etc.



Yard Waste
Leaves, twigs,
grass, etc.



E-Waste
Phones, TVs,
laptops, etc.



Tanglers
Hoses, hangers, wire, string
lights, extension cords, etc.



HHW
Paint, cleaners,
pesticides, etc.



Batteries
Alkaline,
lithium-ion, etc.



Polystyrene Foam
"Styrofoam", packing
peanuts, takeout boxes, etc.



Paper Shreds
Use RRRASOC
shredder instead



**Waxed
Cardboard**
Freezer boxes



**Paper Towels, Facial
Tissue, Napkins, or
Toilet Paper**



Medical Waste
Needles, syringes,
pills, etc.



Food Waste
Fruits, veggies,
meat, etc.

DID YOU KNOW?

RRRASOC services the following member communities:

Farmington

Farmington Hills

Milford

Milford Township

Novi

Southfield

South Lyon

Walled Lake

Wixom
